Kaneda Fabrication Works (fictional)

POSTWELD HEAT TREATMENT RECORD

Job 26-118 · Vessel V-110 · Drawing HBK-PV-110 rev B

Load no.	**L-01**
Furnace	**F-2 (gas fired)**
Date	**2026-10-10**
Procedure	**HT-PROC-03 rev 2**

LOAD

Items in load	Governing thickness
Vessel V-110 complete: joints W-11, W-12, W-14, W-15	**20 mm**
Required (WPS-07 / drawing)	Thermocouples
620 ± 15 °C, 1 h per 25 mm, 15 min minimum = 48 min	**4 (TC1-TC4), on the vessel**

RECORDED CYCLE

Stage	Requirement (UCS-56(d))	Recorded
Loading temperature	425 °C maximum	300 °C
Heating rate above 425 °C	222 °C/h maximum (222 x 25 / t, 222 max.)	150 °C/h
Soak temperature	605 - 635 °C	620 °C (TC range 612 - 626 °C)
Holding time at soak	48 min minimum	35 min
Cooling rate above 425 °C	278 °C/h maximum	180 °C/h
Below 425 °C	-	Still air

CHART (TC average, °C vs h)

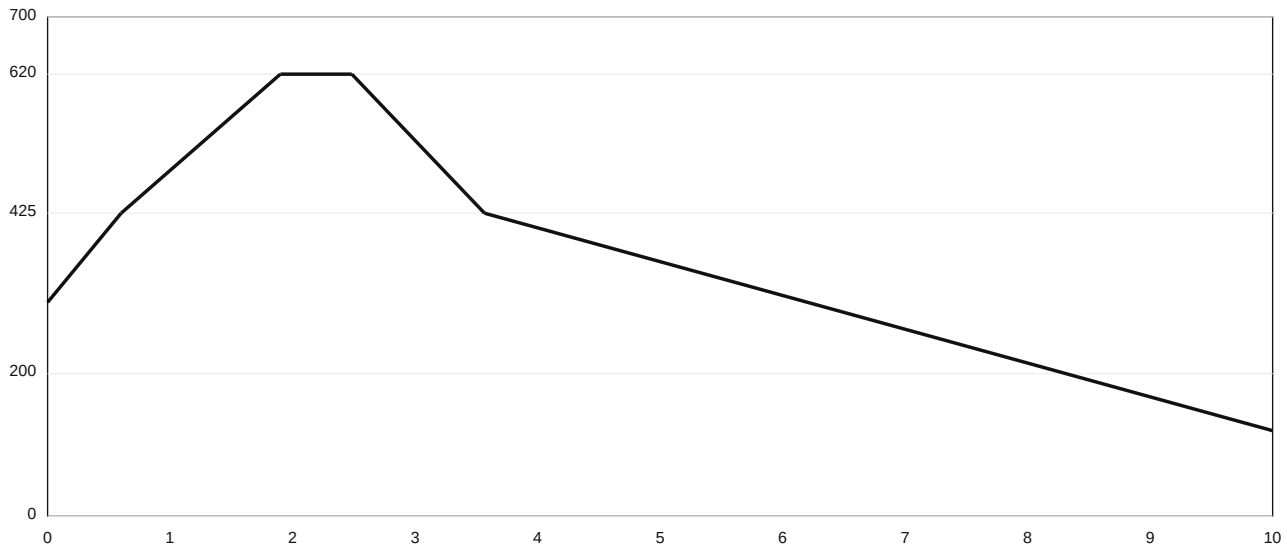

Heat treatment operator	QC manager
D. Kowalski (fictional)	**L. Ortega (fictional)**
signed D. Kowalski 2026-10-10	*signed L. Ortega* 2026-10-11

SYNTHETIC DOCUMENT - generated for software testing - not a real record
